

Project scope

Everything listed under "In the build" is delivered as part of this project, covered by the Rs 1,25,000. Nothing here is held back for a later version.



In the build

THE APPS

- ✓ Android app, live on Google Play
- ✓ iPhone app, live on the App Store
- ✓ Brand website

THE VASTU ENGINE

- ✓ 143 rules, every room mapped to its zone on the 81-pada grid
- ✓ Instant score with a colour-coded zone map
- ✓ Plain-language defect report, ranked by severity
- ✓ What to change on the plan, plus remedies for what cannot move
- ✓ Flat and apartment analysis
- ✓ 8-zone, 16-zone and 45-devata grid systems

READING THE PLAN

- ✓ AI-assisted floor-plan reading - the app reads it, you confirm it
- ✓ Guided grid for any plan the AI cannot read cleanly
- ✓ Live phone compass for setting direction on site

AROUND IT

- ✓ AI Vastu assistant, answering from our own knowledge base
- ✓ Remedy store with Razorpay payments
- ✓ English, Hindi, Tamil, Telugu, Marathi and Bengali
- ✓ App and website design - three concepts, you choose one
- ✓ Product and technical advice through the build, ending at launch




Not in the build

- Marketing, growth and ad spend - yours to run
- All running costs - listed on page 4
- Human Vastu consultations - not part of this build
- Anything not listed above - quoted in writing before work starts

The timeline

Two months. Week 1 begins Monday 20 July 2026, with everything delivered by around Sunday 20 September 2026. Android lands first, on 4 August.

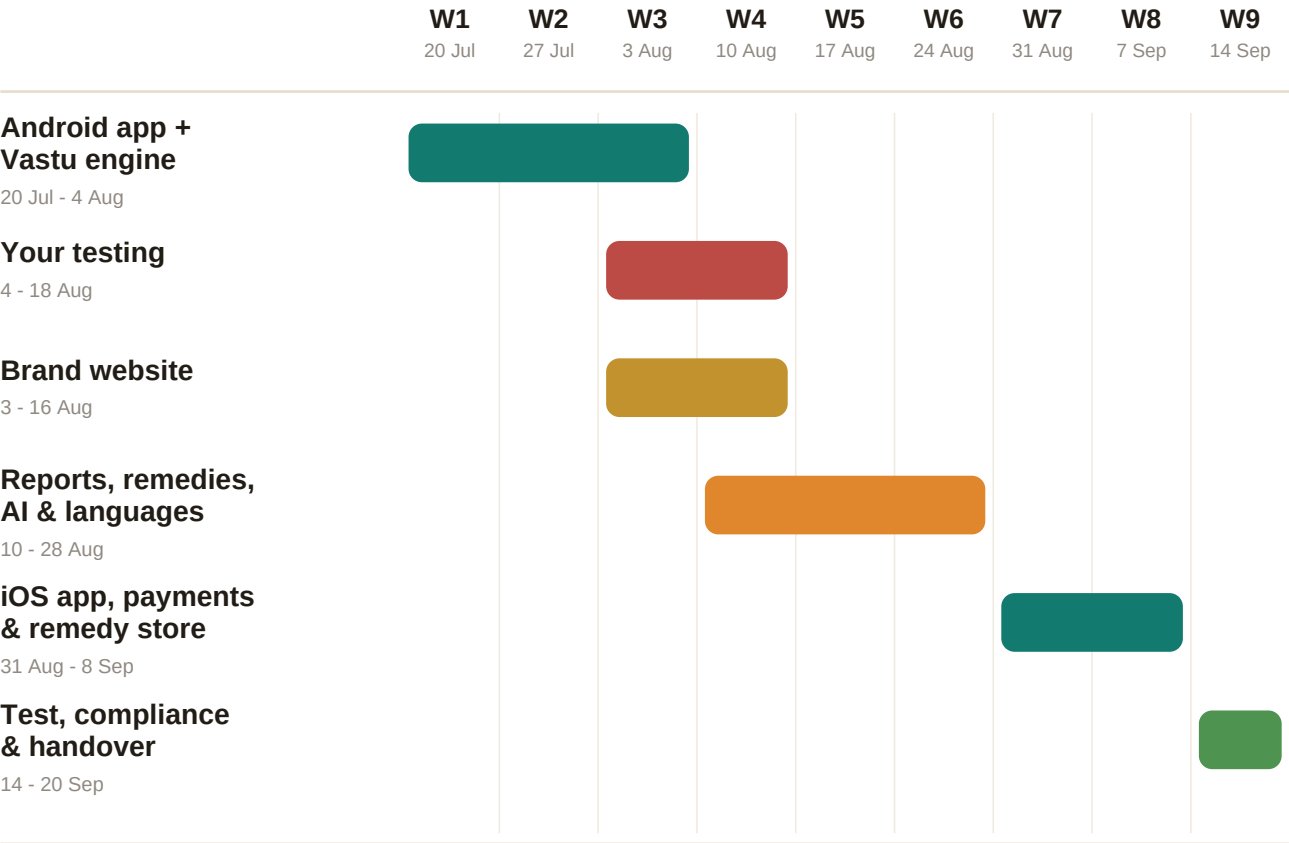

Delivered so far

- 17 July - Vastu rules engine, for your expert review awaiting your feedback
- 17 July - Working prototype of the app, for review awaiting your feedback
- 23 July - Colour concepts shared; you chose Sage & Gold agreed

Key dates

- 4 August - Android app with the full Vastu engine, on your phone
- 4-18 August - You test it. The website is built in parallel.
- 20 September - Everything delivered: both apps submitted, website live



We review together at 11am every Sunday

That standing call is where decisions get made. If something we need is not back within 48 hours, we make the call ourselves, write it down, and keep building to the date. That documented decision then counts as approved - changing it afterwards is a change request. **Silence won't move the project delivery.**

Dependencies

Two kinds. The first we can work around and still hit the date.

The second has no workaround - if these are late, the launch moves.



No workaround exists

These are accounts and credentials. We cannot build our way past them.

Razorpay business registration + KYC

1-3 weeks. Without live keys the store cannot take a single payment.

Google Play developer account, in your name

We cannot submit the Android app without it.

Apple Developer account, in your name

We cannot submit the iPhone app. Business enrolment needs a D-U-N-S number - start now.

A business Google account

Everything above is created from it. Set this up first.



We work around these

If these are late, we decide, document it, and keep to the date.

- ✓ Confirm the app name, and buy the domains
- ✓ Design concept - decided: Sage & Gold, 23 Jul
- ✓ Sign off the Vastu rules the engine is built on
- ✓ Legal pack: disclaimer, privacy policy, terms, refunds
- ✓ Launch languages and the free-vs-paid split
- ✓ Website copy and images, remedy products and prices
- ✓ Two weeks of testing on the Android build, from 4 August



One decision-maker

If there are two opinions in the room with no tie-breaker, everything gets built twice and only one of them gets paid for.

Payments and running costs

Rs 1,25,000 in five stages. Each stage is demonstrated and signed off before the next begins. Payment due within 7 days of sign-off.

Stage 1 · Design & setup Rs 10,000 paid 17 Jul · Rs 15,000 due today, 25 Jul	Rs 25,000
Stage 2 · Android app + Vastu engine On delivery, 4 August 2026	Rs 35,000
Stage 3 · Reports, remedies, AI & languages Sign-off, around 28 August 2026	Rs 30,000
Stage 4 · iOS app, payments & remedy store Sign-off, around 8 September 2026	Rs 20,000
Stage 5 · Store submission & handover On delivery, around 20 September 2026	Rs 15,000
Total	Rs 1,25,000



After delivery - Rs 3,000 a month, first month free

First month after delivery is free, then Rs 3,000 a month for bug fixes, stability and minor in-scope changes. This replaces the 5% revenue royalty - I have opted out, so you keep 100% of what the apps earn.

Your running costs

Paid directly by you, not part of the Rs 1,25,000. Figures are indicative.

Google Play developer account	Rs 2,100	one-off
Apple Developer Program	Rs 8,300	every year
Domains · .com + .in	Rs 1,500	every year
Database & hosting	free to start	then ~Rs 2,100/mo
AI · Vastu assistant	per use	from launch
AI · floor-plan reading	per use, higher	from launch
Razorpay	~2% + GST	per sale
Ad budget	your call	ongoing



The AI cost is the one that grows

Store fees and hosting are flat. AI is charged per use, so it rises with every report. Floor-plan reading costs materially more per use than the text assistant, because images cost far more to process than words.
