



VastuFirst

8 weeks to both app stores

Android · iPhone · Website

A simple week-by-week plan: what gets built, what we need from you, when each payment is due, and when it goes live.

At a glance



WHAT WE BUILD

Two apps, a website, and the Vastu engine behind them



HOW LONG

8 weeks, in 5 phases



HOW WE WORK

A demo you can open, and one update, every week



YOUR RUNNING COSTS

Hosting, store fees, AI usage and ad budget sit with you



Week 8 is a launch, not the finish

You get a strong, genuinely useful first version live on both stores. A few extras are saved for version 2 - shown on page 8. A lean, excellent launch beats a bloated one that slips.



Two things from you decide the date

Start the Razorpay payment paperwork on day one (it can take 1-3 weeks), and turn decisions around within 48 hours. Everything else, we control. These two, we don't - so they're where a delay would come from.

The 8 weeks



Design & setup

Week 1

The look, the screens, the onboarding, and the website design. You get three design concepts to choose from, then a clickable app you can tap through - real screens, logic comes next.

✓ **You can see:** the full app design, on your own phone.



The Vastu engine

Weeks 2-4

The heart of it. Upload or draw a plan, mark North, and every room maps to its zone. The engine scores the home and finds the defects. The biggest phase.

✓ **You can see:** your own home scored and its defects flagged - live, on Android and iPhone.



Reports, remedies & AI

Weeks 5-6

The full report: what to change, and remedies for what can't move. Plus the AI assistant that answers Vastu questions from our own knowledge base.

✓ **You can see:** the whole journey - free score, then the full paid report.



Payments, store & website

Week 7

Razorpay wired in so users can pay. The remedy store. The brand website, built and live.

✓ **You can see:** a user pay, get their report, and buy a remedy. The website is up.



Test & launch

Week 8

Testing on real phones. Bug fixes. Disclaimer, privacy policy and terms in place. Both apps submitted, website live.

✓ **You can see:** VastuFirst live on both stores.




The one date nobody controls

Apple reviews every app before it goes live - usually 1 to 3 days. We submit early to stay safe, but the final iPhone go-live is Apple's call, not ours.

The timeline

Week 1 begins Monday 20 July 2026. Both apps are submitted in Week 8 - on the stores around Sunday 13 September 2026.

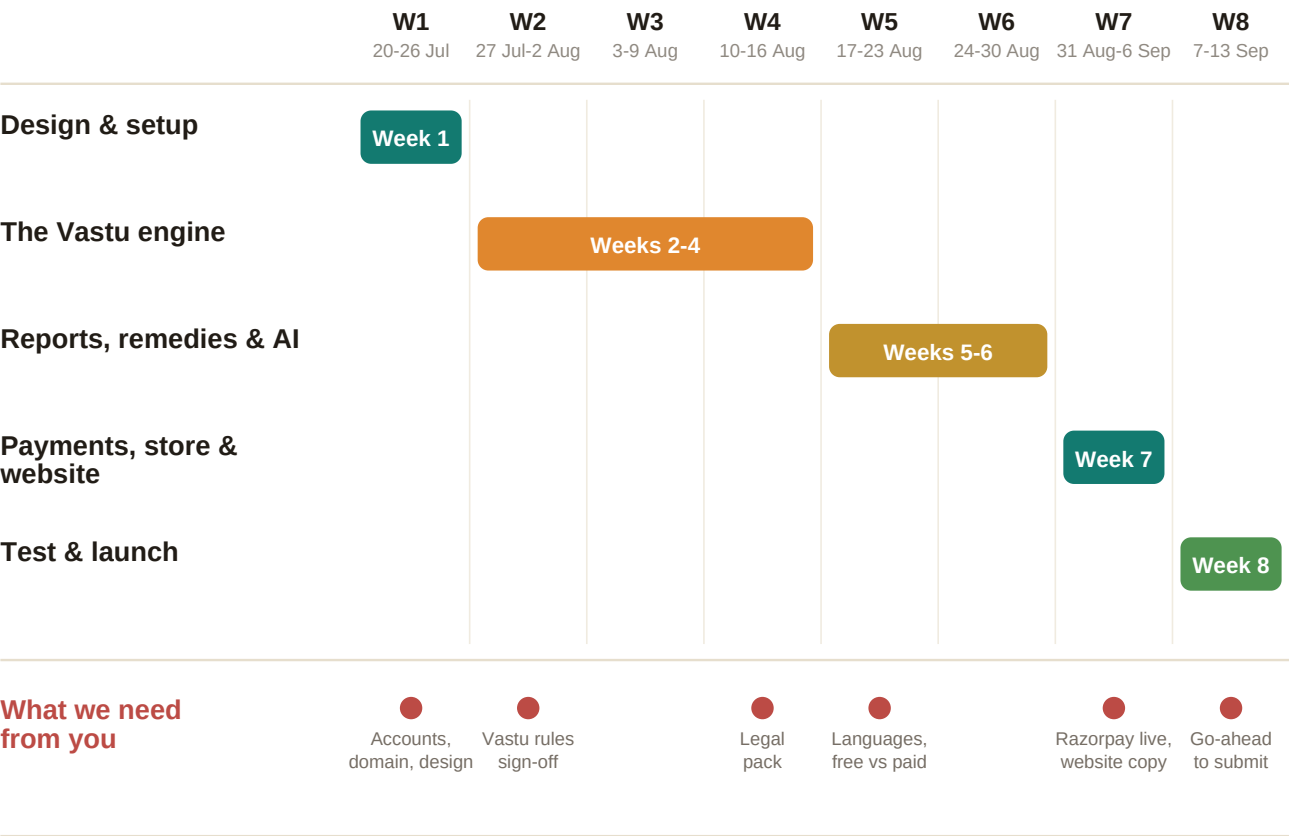

If a week slips, this is what moves

Eight weeks assumes nothing blocks us. If it tightens, we protect the engine and the report - they are the product - and move these, in this order: regional languages first, then the remedy store, then the AI assistant. All three can follow within weeks of launch. Agreeing the order now means no argument later.

What we need from you

Ten things. The three marked in red genuinely decide the launch date.

NOW

A business Google account, in your name

Everything hangs off it - Play Store, Apple, Razorpay, the domain, the database. Set up before anything else, or the handover gets messy.

NOW

Razorpay: business registration + KYC

Takes 1-3 weeks and cannot be rushed. Blocks Week 7. The single most likely cause of a delay.

DAY 1

Confirm the app name, then buy the domains

vastufirst.com and vastufirst.in. Blocks the website, your email addresses, and both store listings.

WEEK 1

Open Google Play and Apple Developer accounts

In your name. Roughly Rs 2,000 one-off and Rs 8,300 a year. Blocks Week 8. Apple business enrolment needs a D-U-N-S number - start early.

WEEK 1

Choose one of the three design concepts

You get three to pick from. Blocks Week 2 onward - the whole app is built on the one you choose.

WEEK 2

Sign off the Vastu rules the engine is built on

Blocks the engine, which is the biggest phase. Changing the rules after it is built means building it twice.

WEEK 4

Legal pack: disclaimer, privacy policy, terms, refunds

Blocks Week 8. Both stores refuse a submission without a live privacy policy link, so this needs the domain and the website already up.

WEEK 5

Confirm launch languages and the free-vs-paid split

Blocks the report and the paywall - we cannot build the paid tier until we know where the line sits.

WEEK 7

Razorpay live. Website words and images. Remedy products and prices.

Blocks Week 7 go-live. The store cannot open without products and prices.

WEEK 8

Final go-ahead to submit, and sign off the legal text

Blocks launch itself.



Two standing commitments

48-hour turnaround on anything the build is waiting on. And one decision-maker - if there are two opinions in the room, everything gets built twice.

Payments

Rs 1,25,000 in five phases. Each phase is demonstrated and signed off before the next one begins. Payment due within 7 days of sign-off.

PHASE 1	PART PAID
Design & setup	Rs 25,000
Rs 10,000 received 17 July 2026 Rs 15,000 due 25 July 2026	
PHASE 2	ON SIGN-OFF
The Vastu engine	Rs 35,000
End of Week 4 · around 16 August 2026	
PHASE 3	ON SIGN-OFF
Reports, remedies & AI	Rs 30,000
End of Week 6 · around 30 August 2026	
PHASE 4	ON SIGN-OFF
Payments, store & website	Rs 20,000
End of Week 7 · around 6 September 2026	
PHASE 5	ON LAUNCH
Test & launch	Rs 15,000
End of Week 8 · around 13 September 2026	
Total	Rs 1,25,000



After launch

Two months of bug fixes included, free. After that, Rs 3,000 a month covers bug fixes and stability, on a 12-month term, up to 4 hours in any month. New features, and updates forced on us by Apple or Google, are quoted separately.



Not included - your running costs

Hosting and database, AI usage, the domain, the Google Play fee (about Rs 2,000 one-off), the Apple Developer Program (about Rs 8,300 a year), and your ad budget. These are paid directly by you and are not part of the Rs 1,25,000.

What launches, what follows



In the launch

- ✓ Android app and iPhone app, both live
- ✓ Upload or draw your plan, mark the direction
- ✓ Every room mapped to its Vastu zone
- ✓ Instant score with a colour-coded map
- ✓ Clear defect report
- ✓ Layout changes, plus remedies
- ✓ AI Vastu assistant
- ✓ Remedy store with payments
- ✓ Brand website · English + Hindi



Version 2

- Automatic plan-reading (v1 uses a quick guided grid)
- More languages - Tamil, Telugu, Marathi, Bengali
- Live phone compass for on-site direction
- Advanced grid systems (16-zone, 45-devata)
- Flat and apartment analysis
- Human consultations, if you want them later

To start the clock

1 Sign the agreement and settle the balance of Phase 1.

2 Start the Razorpay registration the same day.

3 Confirm the app name so we can grab the domains.



Every Friday, you'll know exactly where things stand

One update a week: what shipped, what's next, and anything waiting on you.
No surprises. That's the whole method.
